


**Zoo Interchange Addendum #1**

**1060-33-77 Greenfiled Avenue Bridge - All Activities**

Activity ID	Activity Name	OD	RD	% Comp	Start	Finish	Total Float	2013											
								Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
<b>Zoo Interchange Addendum #1</b>		99	76	23.23%	17-Jan-13 A	12-Jul-13	4												
<b>MILWAUKEE COUNTY</b>		99	76	23.23%	17-Jan-13 A	12-Jul-13	4												
<b>ZOO INTERCHANGE</b>		99	76	23.23%	17-Jan-13 A	12-Jul-13	4												
<b>Greenfield Avenue Bridge</b>		99	76	23.23%	17-Jan-13 A	12-Jul-13	4												
<b>Construction</b>		68	68	0%	16-Mar-13	12-Jul-13	4												
<b>R 40-524 Secant Pile-Schlinger Ave.</b>		68	68	0%	16-Mar-13	12-Jul-13	4												
<b>Wall Work</b>		68	68	0%	16-Mar-13	12-Jul-13	4												
R524-3010	R524: Temporary Shoring	8	8	0%	16-Mar-13	28-Mar-13	4												
R524-3020	R524: Misc. Removals & Existing Concrete Abutment	5	5	0%	29-Mar-13	05-Apr-13	4												
R524-3030	R524: Build Drill Bench	4	4	0%	08-Apr-13	11-Apr-13	4												
R524-3040	R524: Guide Wall	4	4	0%	12-Apr-13	16-Apr-13	4												
R524-3050	R524: Secants 1-39	20	20	0%	17-Apr-13	13-May-13	4												
R524-3060	R524: Secant Cap	3	3	0%	15-May-13	17-May-13	4												
R524-3070	R524: Excavate Face of Secants	8	8	0%	20-May-13	31-May-13	4												
R524-3080	R524: Structure Excavation MSE Wall Footing/Leveling Pad - ...	3	3	0%	03-Jun-13	05-Jun-13	4												
R524-3090	R524: MSE Wall Panels & Backfill - Unit 3	10	10	0%	07-Jun-13	24-Jun-13	4												
R524-3110	R524: Coping	4	4	0%	25-Jun-13	01-Jul-13	4												
R524-3120	R524: Railing	3	3	0%	02-Jul-13	08-Jul-13	4												
R524-3130	R524: Stripping	3	3	0%	09-Jul-13	12-Jul-13	4												
<b>Utility Delays</b>		23	8	65.22%	17-Jan-13 A	15-Mar-13	3												
A-1030	Schlinger Avenue Utility Delays	23	8	65.22%	17-Jan-13 A	15-Mar-13	3												

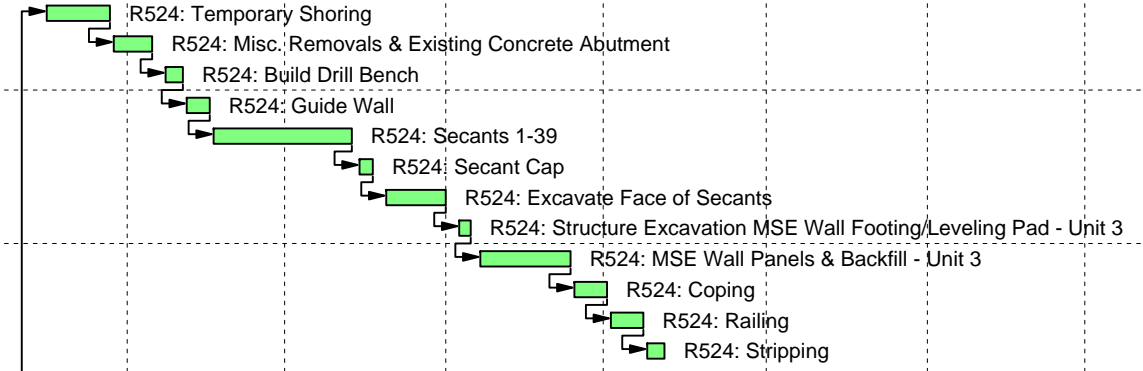

■ Remaining Level of Effort   
 ■ Actual Work  
■ Actual Level of Effort   
 ■ Remaining Work

**Zignego Company**

Project ID: GFA UP 01  
TASK filter: (Untitled Filter).
