


STH 57 - Village of Brown Deer and City of Mequon 2150-00-72 - STH 57 Brown Deer Rd - Float Path to Complete STH 57 and STH 100 to Stage 6

Activity ID	Activity Name	OD	RD	% Comp	Start	Finish	Total Float	2022					2023
								Aug	Sep	Oct	Nov	Dec	Jan
<b>STH 57 - Village of Brown Deer and City of Mequon</b>													
<b>Milestones</b>													
Milestone 1040	Interim Completion Date - Nov 22,2022	0	0	0%	30-Nov-22	30-Nov-22	-8						
<b>Construction</b>													
<b>Stage 3</b>													
<b>Stage 3 HWY 57 (RAB to HWY 100)</b>													
57S_Stage 3 3050	Storm Sewer Pre Bedrock Delay (24 Structures) Genesis	12	0	100%	08-Aug-22 A	12-Sep-22 A							
57S_Stage 3 3080	Bedrock Delay - New Str 223 Lead Time	13	0	100%	24-Aug-22 A	12-Sep-22 A							
57S_Stage 3 3090	Storm Sewer Post Bedrock Delay ( 34 Structures) Genesis	11	11	0%	13-Sep-22 A	27-Sep-22	2						
57S_Stage 3 3060	Base Aggregate (6566 Tons) ZC	3	3	0%	28-Sep-22	30-Sep-22	2						
57S_Stage 3 3070	Electrical Crossings & Loops, Outdoor	3	3	0%	28-Sep-22	30-Sep-22	2						
<b>Stage 5</b>													
<b>Stage 5 HWY 100 WB (Arbon to Killdeer)</b>													
100_Stage 5 5000	Removing Pavement (10,954 SY) ZC	8	8	0%	18-Aug-22 A	22-Sep-22	-3						
100_Stage 5 5030	Storm Sewer (31 Structures) Genesis	7	0	100%	06-Sep-22 A	25-Oct-22	-3						
100_Stage 5 5010	Common Excavation (14,081 CY) ZC	14	14	0%	23-Sep-22	12-Oct-22	-3						
100_Stage 5 5020	Select Crushed Material (14,961 Tons) ZC	8	8	0%	13-Oct-22	24-Oct-22	-3						
100_Stage 5 5040	Base Aggregate (4604 Tons) ZC	3	3	0%	25-Oct-22	27-Oct-22	-3						
100_Stage 5 5060	Pave 17ft STA 483+30 to 506+60 (3500 SY) ZC	4	4	0%	28-Oct-22	02-Nov-22	-3						
100_Stage 5 5050	Pave 24ft STA 483+30 to 506+60 (5267 SY) ZC	5	5	0%	03-Nov-22	09-Nov-22	-3						
100_Stage 5 5070	Concrete Pavement Handpours (3224 SY) ZC	4	4	0%	04-Nov-22	09-Nov-22	-3						
100_Stage 5 5080	Curb & Gutter (2420 LF) Trierweiler	2	2	0%	08-Nov-22	09-Nov-22	-3						
100_Stage 5 5120	Concrete Sidewalk (12,883 SF) Trierweiler	3	3	0%	10-Nov-22	14-Nov-22	-3						
100_Stage 5 5090	Pull Boxes and Bases Deerbrook Int (16 Each) ODL	5	5	0%	10-Nov-22	16-Nov-22	-3						
<b>Stage 5 HWY 57 SB (HWY 100 to Deerwood)</b>													
57N_Stage 5 5110	Stand Poles Deerwood Int (17 Each)	3	3	0%	17-Nov-22	21-Nov-22	-3						
<b>Stage 5 HWY 57 (RAB to HWY 100)</b>													
57S_Stage 5 5000	Pave 24 ft NB&SB STA 104+00 to 119+50 (8266 SY)	5	5	0%	03-Oct-22	07-Oct-22	2						
57S_Stage 5 5010	Pave 17 ft NB&SB STA 104+00 to 119+50 (5855 SY)	3	3	0%	10-Oct-22	12-Oct-22	2						
57S_Stage 5 5020	Pave 24 ft NB Tun Ln STA 117+00 to 119+50 (700 SY)	3	3	0%	13-Oct-22	17-Oct-22	2						
57S_Stage 5 5030	Concrete Pavement Handpours (305 SY)	1	1	0%	18-Oct-22	18-Oct-22	2						
57S_Stage 5 5040	Curb and Gutter (6953 LF) Trierweiler	5	5	0%	19-Oct-22	25-Oct-22	2						
57S_Stage 5 5070	Concrete Sidewalk (13,465 SF) Trierweiler	3	3	0%	21-Oct-22	25-Oct-22	2						
57S_Stage 5 5060	Pull Boxes and Bases 100 Int (17 Each)	6	6	0%	25-Oct-22	01-Nov-22	2						
100_Stage 3 3130	Pull Boxes and Bases 57 Int (10 Each) ODL	3	3	0%	02-Nov-22	04-Nov-22	2						
57S_Stage 5 5080	Topsoil (13,289 SY) ZC	6	6	0%	04-Nov-22	11-Nov-22	2						
57S_Stage 5 5100	Restoration Seed and Erosion Mat (8760 SY)	5	5	0%	08-Nov-22	14-Nov-22	2						
57S_Stage 5 5110	Permanent Signing (54 Signs)	2	2	0%	11-Nov-22	14-Nov-22	2						
57S_Stage 5 5120	Permanent Pavement Marking (Century)	3	3	0%	15-Nov-22	17-Nov-22	2						
<b>Stage 5-6 Winter Shutdown</b>													
Stage 5-6 5020	Activate HWY 57 & Deerwood Signals (ODL)	1	1	0%	22-Nov-22	22-Nov-22	-3						
Stage 5-6 5030	Activate HWY 57 & Schroeder Signals (ODL)	1	1	0%	23-Nov-22	28-Nov-22	-3						
Stage 5-6 5040	Open HWY 57 NB&SB Teutona to HWY 100 (CTC)	1	1	0%	28-Nov-22	29-Nov-22	-2						
Stage 5-6 5060	Remove Temp Signals 57 & Deerwood (ODL)	1	1	0%	28-Nov-22	29-Nov-22	-3						
Stage 5-6 5070	Remove Temp Signals 57 & Schroeder (ODL)	1	1	0%	29-Nov-22	30-Nov-22	-3						

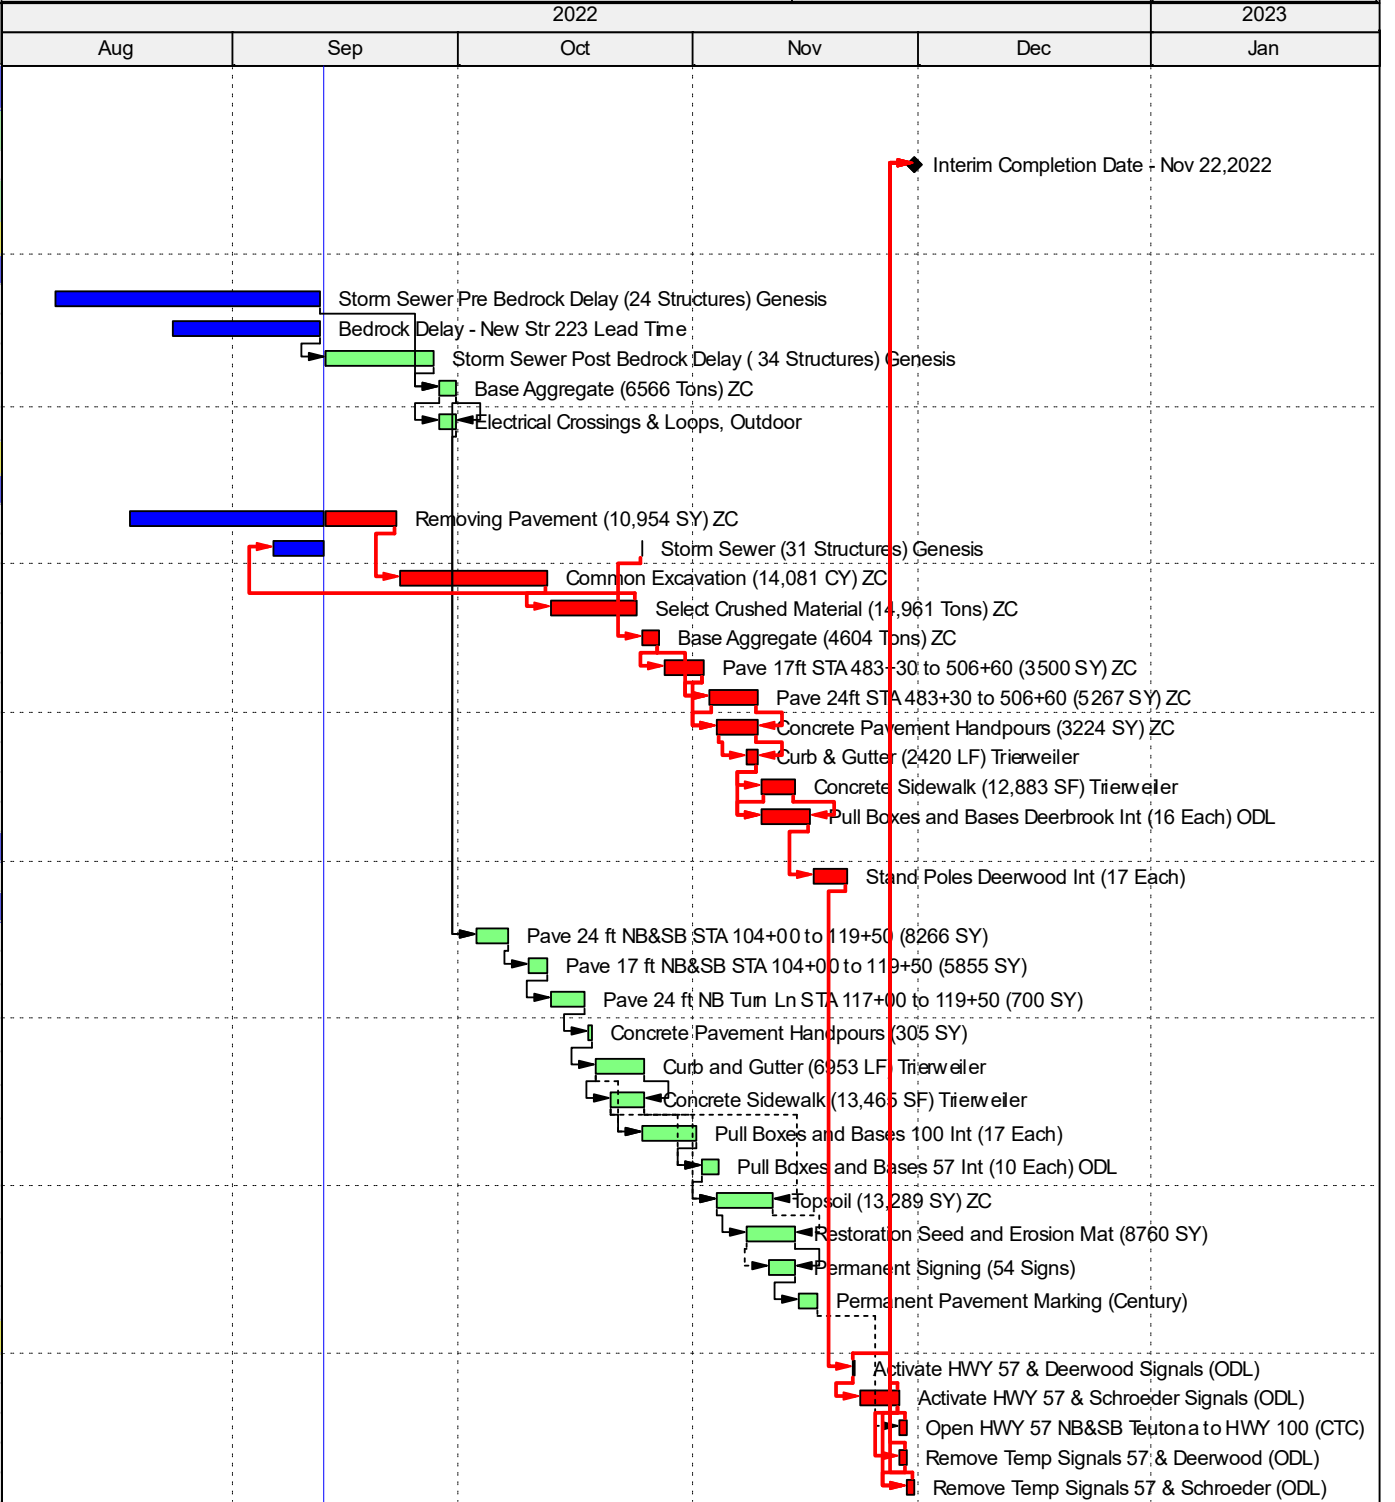

■ Actual Work     ■ Critical Remaining Work  
■ Remaining Work     ◆ Milestone
